

Priliminary Project Schedule

Activity ID	Activity Name	Org Dur	Rem Dur	Start	Finish	2016												2017											
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep			
Westmont IGLL		413	413	15-Dec-15 A	17-Aug-17																								
Summary & Milestones		383	383	19-Jan-16	20-Jul-17																								
Permits		40	25	15-Dec-15 A	08-Feb-16																								
Estimating & GMP Preperation		51	51	18-Jan-16	28-Mar-16																								
Subcontractor Buyout		65	65	29-Mar-16	28-Jun-16																								
Submittals & Procurement		125	125	25-Apr-16	20-Oct-16																								
Construction		348	348	05-Apr-16	17-Aug-17																								
Mobilization & Site Preparation		20	20	05-Apr-16	02-May-16																								
MS1030	Mobilize Site Trailers	5	5	05-Apr-16	11-Apr-16																								
MS1040	ID Trees for Protection	5	5	12-Apr-16	18-Apr-16																								
MS1050	MEP for Const. Trailers	5	5	12-Apr-16	18-Apr-16																								
MS1060	Site Survey (Est. Control & Layout)	5	5	12-Apr-16	18-Apr-16																								
MS1070	Site Fencing & Construction Signage	5	5	12-Apr-16	18-Apr-16																								
MS1080	Install Root Protection @ ID Trees	5	5	19-Apr-16	25-Apr-16																								
MS1090	Set Up SWPP (Erosion, & Sediment Control)	5	5	26-Apr-16	02-May-16																								
South Resident Hall		321	321	03-May-16	08-Aug-17																								
Site Work & Utilities		25	25	03-May-16	07-Jun-16																								
SR2040	Cut & Remove Existing Trees	5	5	03-May-16	09-May-16																								
SR2050	Rough Grade / Clear & Grub	5	5	10-May-16	16-May-16																								
SR2060	Establish Sub-grade	5	5	17-May-16	23-May-16																								
SR2070	Install Underground Utilities	10	10	24-May-16	07-Jun-16																								
Foundation / SOG		53	53	24-May-16	08-Aug-16																								
SR1910	Layout Caissons	3	3	24-May-16	26-May-16																								
SR1920	Drill & Place Caissons	10	10	27-May-16	10-Jun-16																								
SR1930	Elevator Pits	10	10	27-Jun-16	11-Jul-16																								
SR1940	Undergroud MEP Trades	10	10	14-Jun-16	28-Jun-16																								
SR1950	Install Gabion Walls	10	10	13-Jun-16	24-Jun-16																								
SR1960	Form & Pour Column Caps	10	10	13-Jun-16	24-Jun-16																								
SR1970	Grade Bottom of Slab	3	3	27-Jun-16	29-Jun-16																								
SR1980	Under SOG Waterproofing / Barrier	3	3	12-Jul-16	14-Jul-16																								
SR1990	Formwork & Embeds	5	5	30-Jun-16	07-Jul-16																								
SR2000	Reinforcing SOG	7	7	15-Jul-16	25-Jul-16																								
SR2010	Place Concrete SOG	5	5	26-Jul-16	01-Aug-16																								
SR2020	S/F/F Slab on grade	5	5	26-Jul-16	01-Aug-16																								
SR2030	Form & Pour Stem Walls	5	5	02-Aug-16	08-Aug-16																								
Building Structure & Exterior		122	122	09-Aug-16	02-Feb-17																								
SR1660	Layout & Anchor Bolt Adjustment	5	5	09-Aug-16	15-Aug-16																								
SR1670	Frame 1st Level	12	12	16-Aug-16	31-Aug-16																								
SR1680	Shear, Plumb & Line 1st Level	5	5	01-Sep-16	08-Sep-16																								
SR1690	Stack & Roll Joist 2nd Level	5	5	09-Sep-16	15-Sep-16																								
SR1700	Deck (Plywood) 2nd Level	5	5	16-Sep-16	22-Sep-16																								
SR1710	Block & Pick Up 1st Level	5	5	09-Sep-16	15-Sep-16																								
SR1720	Layout 2nd Level	2	2	23-Sep-16	26-Sep-16																								
SR1730	Stairs & Railings	5	5	27-Sep-16	03-Oct-16																								
SR1740	Frame 2nd Level	12	12	27-Sep-16	12-Oct-16																								
SR1750	Shear, Plumb & Line 2nd Level	5	5	13-Oct-16	19-Oct-16																								
SR1760	MEP Rough-in	20	20	29-Sep-16	26-Oct-16																								
SR1770	Stack & Roll Joist Roof	5	5	20-Oct-16	26-Oct-16																								
SR1780	Erect Scaffolding	5	5	20-Oct-16	26-Oct-16																								
SR1790	Deck (Plywood) Roof	5	5	27-Oct-16	02-Nov-16																								
SR1800	Exterior Sheathing & Waterproofing	7	7	03-Nov-16	14-Nov-16																								
SR1810	Windows & Exterior Door Frames	7	7	15-Nov-16	23-Nov-16																								

- Mobilize Site Trailers
- ID Trees for Protection
- MEP for Const. Trailers
- Site Survey (Est. Control & Layout)
- Site Fencing & Construction Signage
- Install Root Protection @ ID Trees
- Set Up SWPP (Erosion, & Sediment Control)
- Cut & Remove Existing Trees
- Rough Grade / Clear & Grub
- Establish Sub-grade
- Install Underground Utilities
- Layout Caissons
- Drill & Place Caissons
- Elevator Pits
- Undergroud MEP Trades
- Install Gabion Walls
- Form & Pour Column Caps
- Grade Bottom of Slab
- Under SOG Waterproofing / Barrier
- Formwork & Embeds
- Reinforcing SOG
- Place Concrete SOG
- S/F/F Slab on grade
- Form & Pour Stem Walls
- Layout & Anchor Bolt Adjustment
- Frame 1st Level
- Shear, Plumb & Line 1st Level
- Stack & Roll Joist 2nd Level
- Deck (Plywood) 2nd Level
- Block & Pick Up 1st Level
- Layout 2nd Level
- Stairs & Railings
- Frame 2nd Level
- Shear, Plumb & Line 2nd Level
- MEP Rough-in
- Stack & Roll Joist Roof
- Erect Scaffolding
- Deck (Plywood) Roof
- Exterior Sheathing & Waterproofing
- Windows & Exterior Door Frames


- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

Westmont College IGLL
Project Schedule

data date: 05-Jan-16

Priliminary Project Schedule

Activity ID	Activity Name	Org Dur	Rem Dur	Start	Finish	2016												2017											
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep			
Site Work																													
SW1150	Layout & Stake Hardscape	3	3	10-Feb-17	17-May-17																								
SW1160	Grade for Hardscape	15	15	15-Feb-17	07-Mar-17																								
SW1170	Install Formwork	15	15	22-Feb-17	14-Mar-17																								
SW1180	Install Irrigation Sleeves	5	5	22-Feb-17	28-Feb-17																								
SW1190	Install Reinforcing	10	10	01-Mar-17	14-Mar-17																								
SW1200	Place Concrete	10	10	08-Mar-17	21-Mar-17																								
SW1210	Strip Formwork	5	5	17-Mar-17	23-Mar-17																								
SW1220	Construct Rain Gardens	15	15	17-Mar-17	06-Apr-17																								
SW1230	Install Irrigation	15	15	06-Apr-17	26-Apr-17																								
SW1240	Install Trees	10	10	17-Mar-17	30-Mar-17																								
SW1250	Install Plants	15	15	20-Apr-17	10-May-17																								
SW1260	Install Decomposed Granite	15	15	28-Mar-17	17-Apr-17																								
SW1270	Place Mulch	10	10	04-May-17	17-May-17																								
Leed Commissioning & Certification																													
LD1160	LEED Certification	10	10	21-Jul-17	03-Aug-17																								
Closeout																													
CO1170	Warranty & Close Out Binders	30	30	29-Jun-17	10-Aug-17																								
CO1180	Project Completion	0	0		17-Aug-17																								

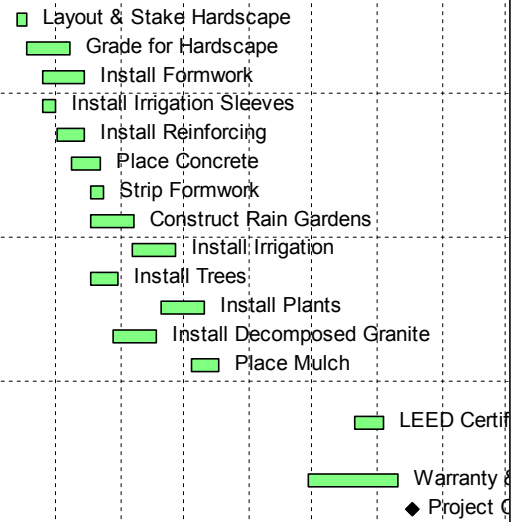

- █ Remaining Level of Effort
- █ Actual Level of Effort
- █ Actual Work
- █ Remaining Work
- █ Critical Remaining Work
- ◆ Milestone
